

Kieling, John, NMENV

From: Migdal, Walter SPA [Walter.Migdal@usace.army.mil]
Sent: Wednesday, August 22, 2012 2:59 PM
To: Moats, William, NMENV
Cc: Kieling, John, NMENV
Subject: KAFB Bulk Fuels Weekly Activity Report attached (UNCLASSIFIED)
Attachments: Weekly Activity Report 22 August 2012.pdf; SVE Schedule 08222012.pdf

Classification: UNCLASSIFIED
Caveats: NONE

Walter Migdal
Project Manager, CESP-PM-ME
Office (505) 343-6297
Cell (505) 301-2923
walter.migdal@usace.army.mil

Classification: UNCLASSIFIED
Caveats: NONE

Weekly Activity Report –Kirtland AFB Bulk Fuels Facility (SS-111, ST-106)

Current Week: 15 August – 22 August 2012

- 15 August – 22 August – Continued soil vapor sampling
- 15 August – 22 August – Continued operation of SVE units (RSI internal combustion engine units) at ST-106 (manifold), KAFB-106149, KAFB-106160, and KAFB-106161.
- 15 August – 22 August – Completed well installation at two intermediate wells (KAFB-106205 and KAFB-106208); started drilling at the shallow wells KAFB-106204 and KAFB-106207
- 21 August – KAFB Citizens Advisory Board meeting
- 22 August - Attend the ABCWUA board meeting

	Completed to date (includes casing placement)	Total Number Planned	Percent Complete
Groundwater Wells	82	87	94.2
Direct Push Soil Sampling (does not include step out sampling)	306	306	100
Direct Push Soil sampling (Step outs – 1 st phase)	18	18	100
Direct Push Soil Sampling (Additional step outs)	TBD	TBD	0

Look Ahead: Week of 22 August – 29 August 2012

- Continue with 3rd Quarter 2012 soil vapor monitoring sampling
- Continuation of SVE unit operation
- Complete drilling and well installation at KAFB-106204 and KAFB-106207; decon, setup, and begin drilling at KAFB-106203


Month Ahead:

- Continue with 3rd Quarter 2012 soil vapor sampling
- Continuation of SVE unit operation
- Continue drilling and installing groundwater monitoring wells
- Submit Pre-Remedy Monitoring and Soil Vapor Extraction O&M Plan Addendum

SVE System Status (see attached schedule; updated 6/27/2012)

- System will be ordered from vendor – 10 August 2012
- Submittal of final design letter addendum to the NMED – 10 October 2012
- Installation of utilities (electrical and natural gas) – September/October 2012

- Installation of SVE skids – 15 November 2012
- Emergency Air Permit – in review with AEHD
- Modification to air permit – 14 January 2013

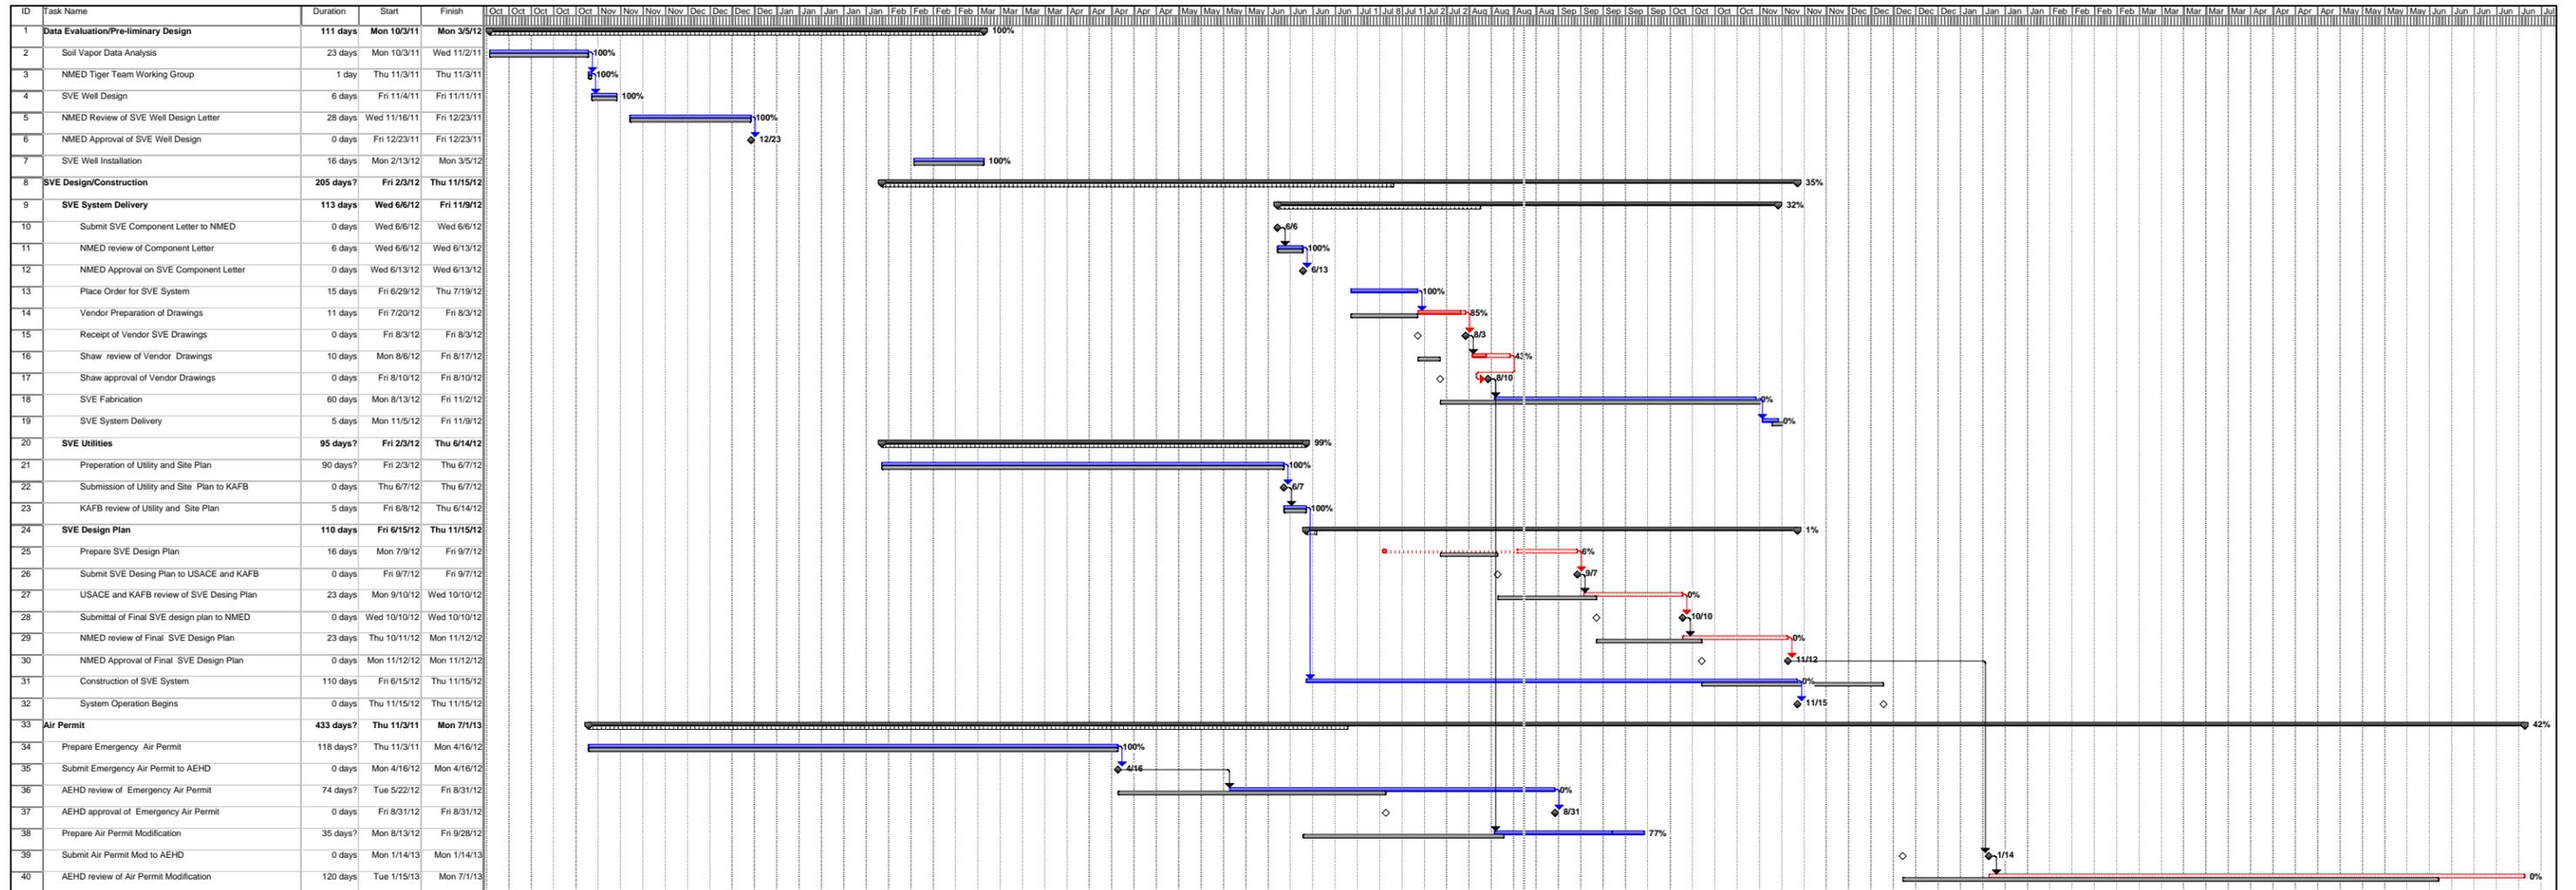

UPDATE: 22 August 2012
NOT FINAL
