

Kieling, John, NMENV

From: Migdal, Walter SPA [Walter.Migdal@usace.army.mil]
Sent: Wednesday, August 29, 2012 5:27 PM
To: Moats, William, NMENV
Cc: Kieling, John, NMENV
Subject: KAFB Bulk Fuels Weekly Activity Report attached (UNCLASSIFIED)
Attachments: Weekly Activity Report 29 August 2012.pdf; SVE Schedule 08292012.pdf

Classification: UNCLASSIFIED
Caveats: NONE

Walter Migdal
Project Manager, CESP-PM-ME
Office (505) 343-6297
Cell (505) 301-2923
walter.migdal@usace.army.mil

Classification: UNCLASSIFIED
Caveats: NONE

Weekly Activity Report –Kirtland AFB Bulk Fuels Facility (SS-111, ST-106)

Current Week: 22 August – 29 August 2012

- 22 August – 29 August – Continued soil vapor sampling
- 22 August – 29 August – Continued operation of SVE units (RSI internal combustion engine units) at ST-106 (manifold), KAFB-106149, KAFB-106160, and KAFB-106161.
- 22 August – 29 August – Completed well installation at shallow well KAFB-106207; continued drilling and started well construction at KAFB-106204

	Completed to date (includes casing placement)	Total Number Planned	Percent Complete
Groundwater Wells ^a	83	87	95.4
Direct Push Soil Sampling (does not include step out sampling)	306	306	100
Direct Push Soil sampling (Step outs – 1 st phase)	18	18	100
Direct Push Soil Sampling (Additional step outs)	TBD	TBD	0

^a Wells reported are specific to those installed on current PBC Contract (2011 and 2012 drilling campaigns; actual number of groundwater wells sampled for characterization is 107 (does not include 9 new monitoring wells)

Look Ahead: Week of 29 August – 5 September 2012


- Continue with 3rd Quarter 2012 soil vapor monitoring sampling
- Continuation of SVE unit operation
- Complete drilling and well installation at KAFB-106204; decon, setup, and begin drilling at KAFB-106203

Month Ahead:

- Submit letter requesting an extension request on delivery date for the Second Quarter 2012 Report (expected delivery date to the NMED – 7 September 2012)
- Submit letter clarifying sampling approach for nine new groundwater monitoring wells (expected delivery date to the NMED – 7 September 2012)
- Continue with 3rd Quarter 2012 soil vapor sampling
- Continuation of SVE unit operation
- Continue drilling and installing groundwater monitoring wells
- Submit Pre-Remedy Monitoring and Soil Vapor Extraction O&M Plan Addendum

SVE System Status (see attached schedule; updated 6/27/2012)

- System ordered from vendor – 10 August 2012
- Submittal of final design letter addendum to the NMED – 10 October 2012
- Installation of utilities (electrical and natural gas) – September/October 2012
- Installation of SVE skids – 15 November 2012
- Emergency Air Permit – in review with AEHD; anticipated approval by end of August
- Modification to air permit – 14 January 2013

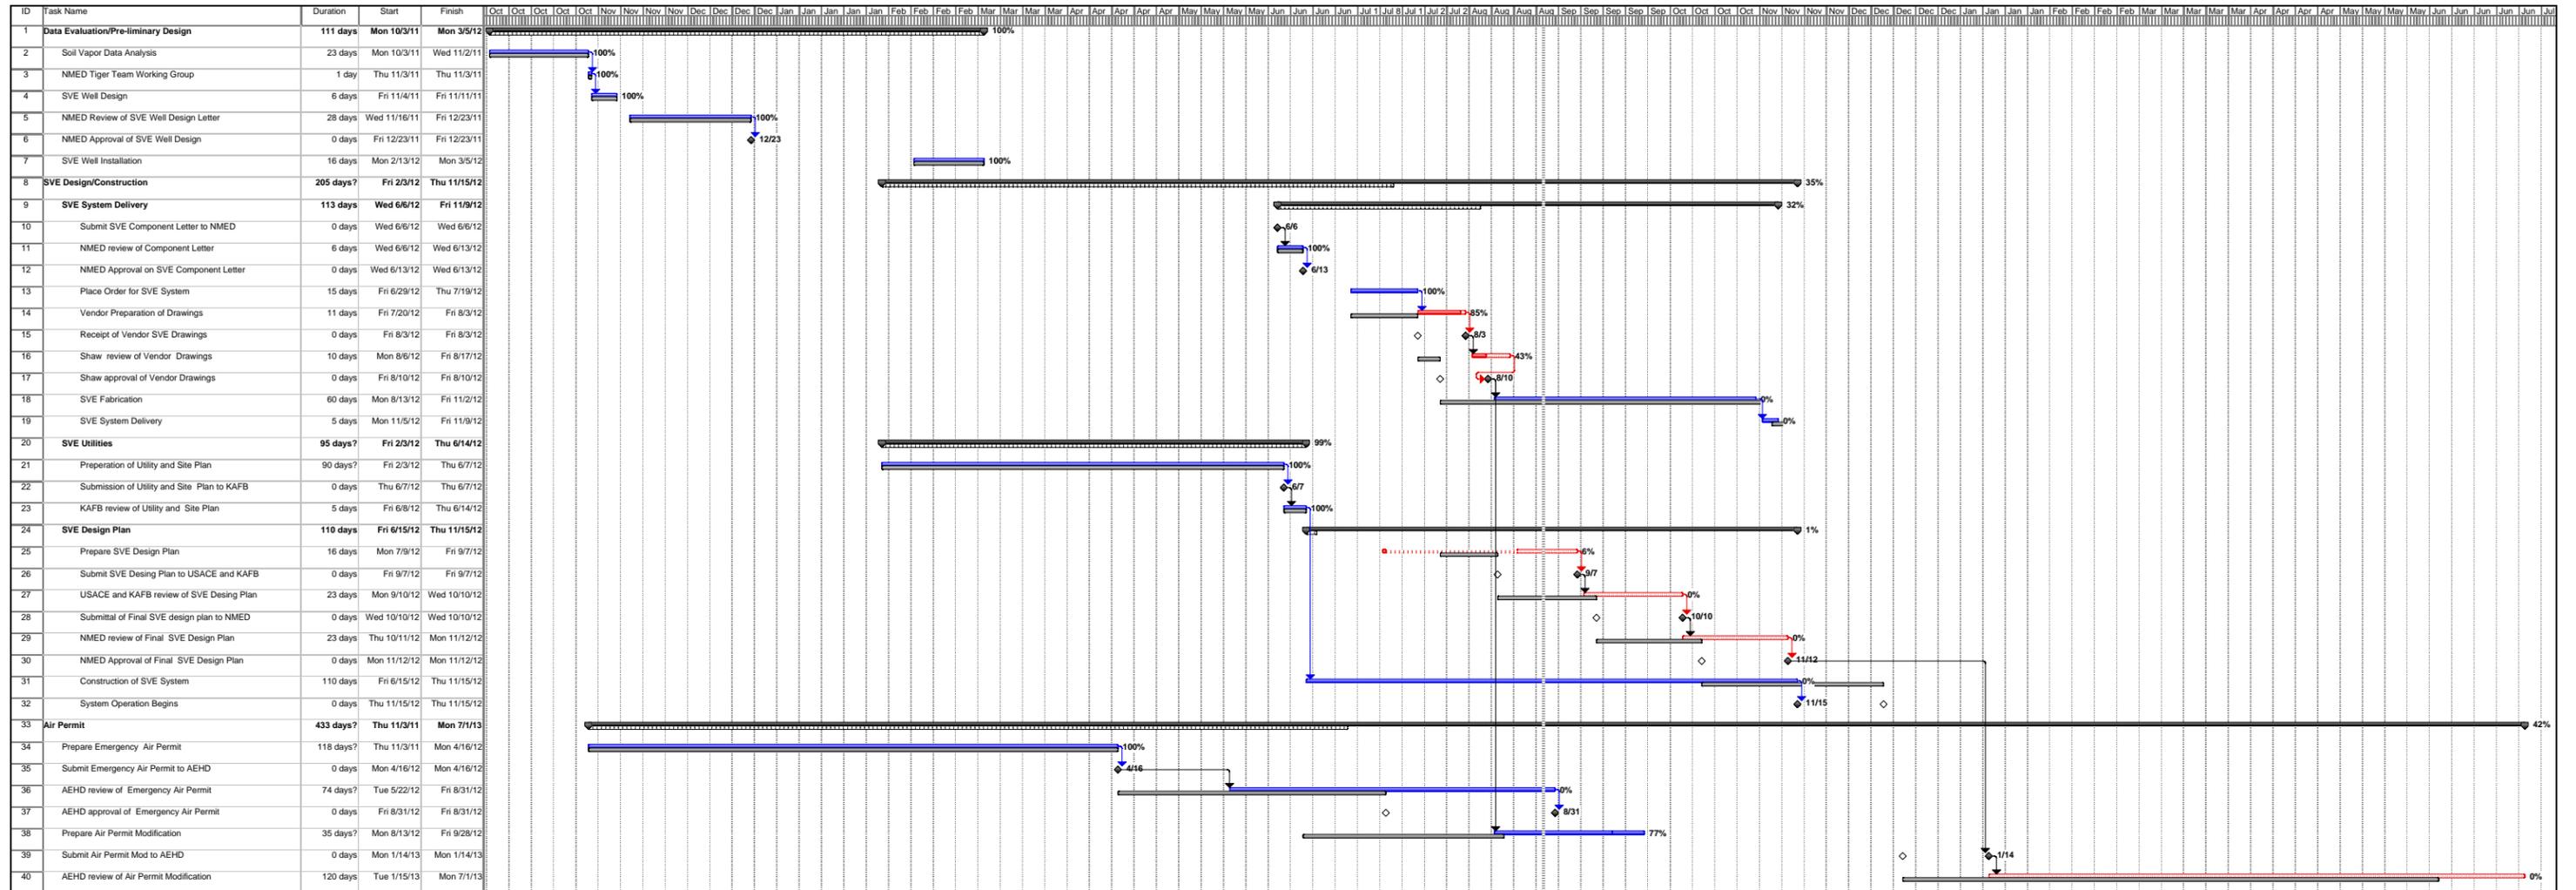

UPDATED: 29 August 2012
NOT FINAL
