

SILVER CITY PROJECT

Location: Corner of 12th St. and Corbin St. in Silver City. From HWY 90, (Hudson St.), turn east on 12th St. until it intersection with Corbin St. The project site is in the stream bottom on the right side of the road. See attached google map.

Approximate Date of Construction Approximately 1998 or 1999.

Number of bales / tires used Approximately 100.

Design information: A concrete foundation was poured, and bales that have been individually wrapped with chicken wire were placed in the wet concrete. After all the bales were placed, the structure was covered with shotcrete. The project is 4 bales high and 100 bales long. The bottom layer is 2 bales deep; the other 3 layers are 1 bale deep.


Cost: Unknown

Other information: The project was constructed on private property under the authority of the Town of Silver City. The design engineer and contractor are unknown.

Photos attached



15 3:27 PM

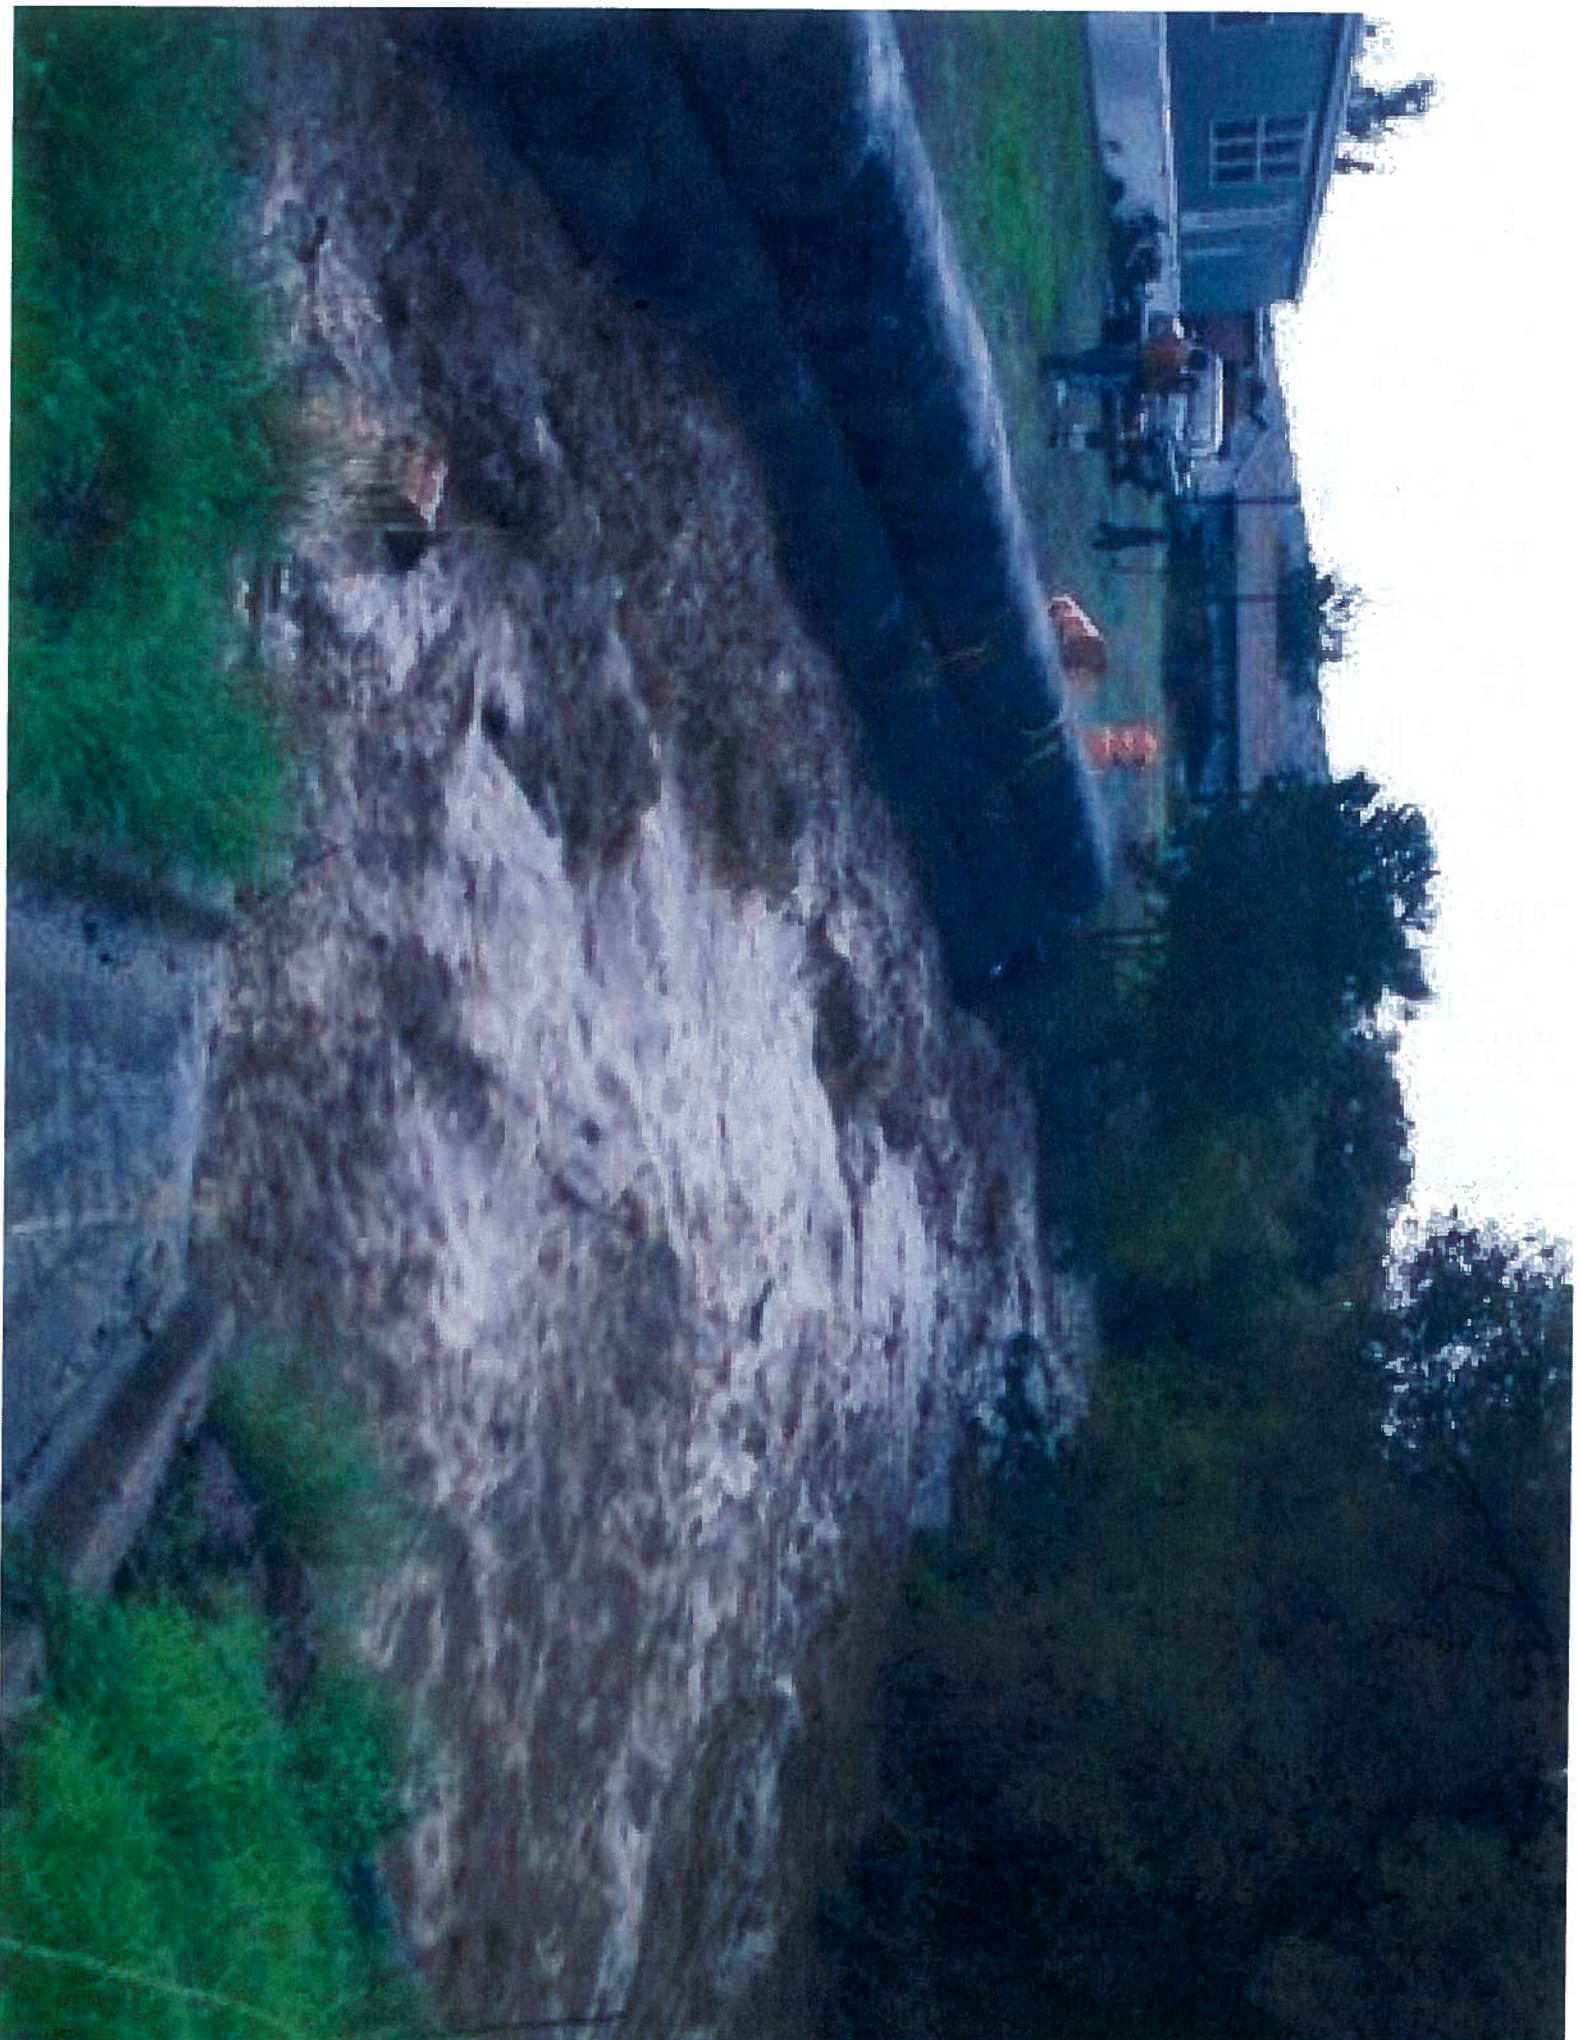




10/12/2011



Address **N Corbin St & E 12th St**
Silver City, NM 88061

Get Google Maps on your phone

Text the word "GMAPS" to 466453

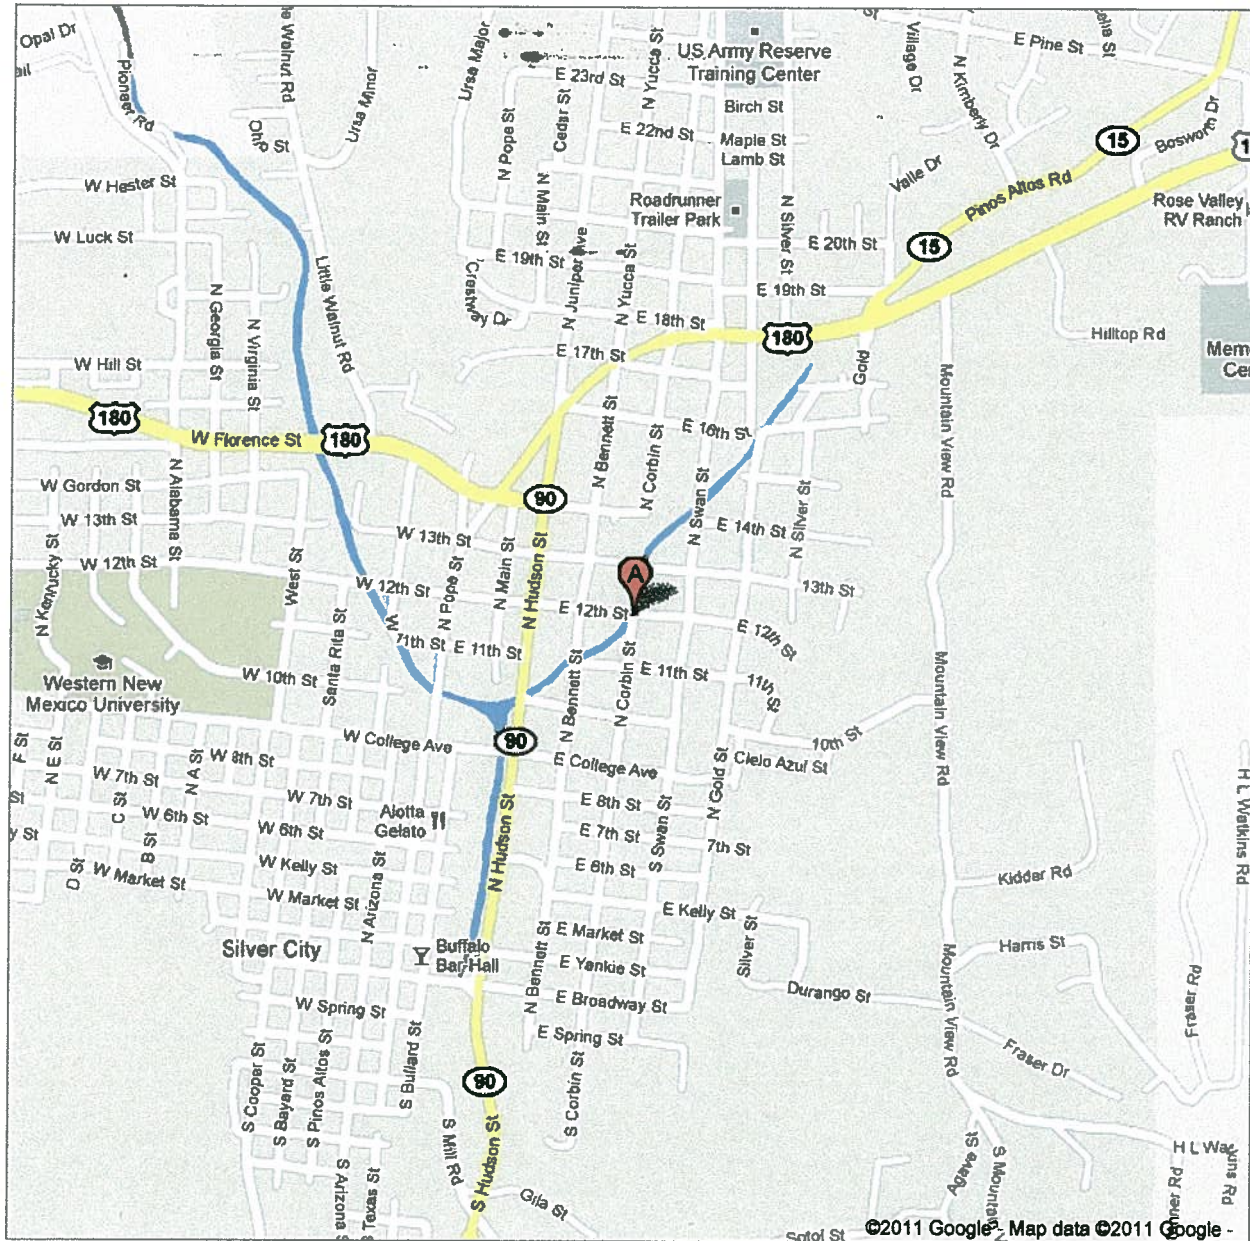

©2011 Google, Map data ©2011 Google
